

Program: FCE2 **Phase:** Engineering Prototype

Date: 15-Jun-20

Status:


Complete: **10%**

Issues:

Workstreams Spotlight:

- 1 SCA P2 Part 6 alternative supplier sourcing
- 2 SCA P2 Part 3 incorp. requested changes
- 3 8D P1 high voltage loss
- 4 Equip. ready test equip. for P2
- 5 Equip. delivery and acceptance of new test stand


Time Plan:

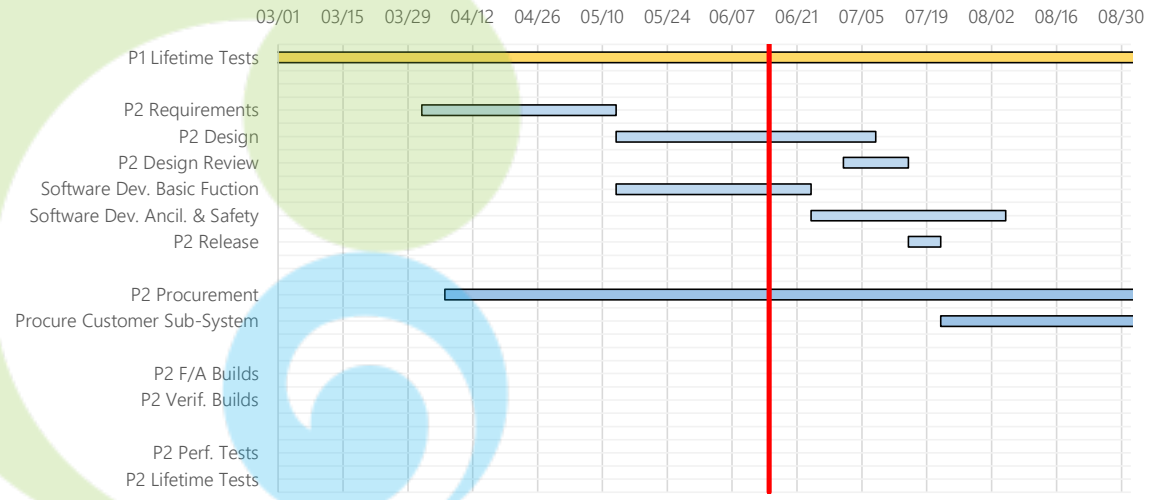

Top NCRs:

- 1 P2 part 6 delivery late +3w
- 2 P2 part 3 delivery late +1w
- 3 P1 life test high voltage loss
- 4 P1 life test inc. sens. in test X
- 5 P2 part 12 supplier quality issue
- 6 P1 part 1 cooling limitation

Budget Performance

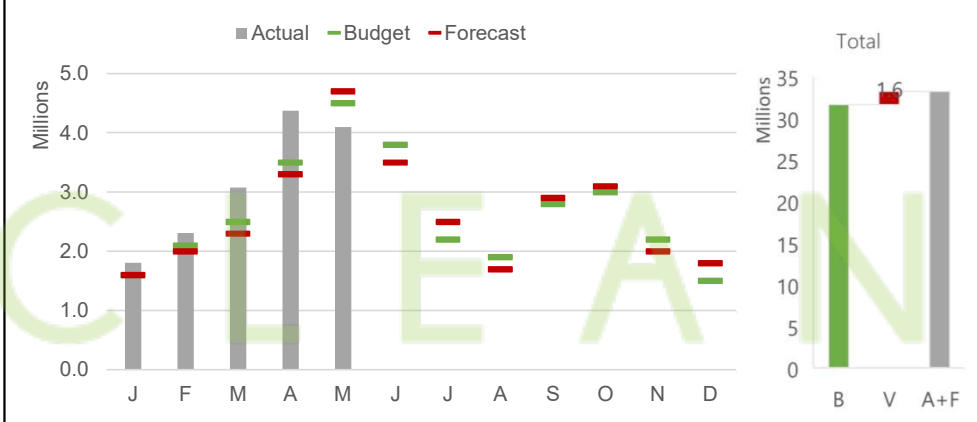

Milestones:

Milestone	CW	Var	WtG
Part 1 PO Released	6	-1	◆
All parts on dock	34	1	11
Customer Sub-System Delivery	33	3	10
P2 Start of Build	36	0	13
Facility Ready	36	0	13
P1 Test Campaign Start	37	0	14
P2 Lifetime Test Complete	38	0	15
P1 Performance Test Complete	40	0	17
P2 Performance Test Start	40	0	17
P2 Lifetime Testing Start	42	0	19
